EARNED VALUE MANAGEMENT REPORT

Clinic Building Extension

Status as of 2026-04-03

OVERALL HEALTH

At risk

CURRENCY	PKR
PROJECT DATES	2026-01-05 to 2026-06-26
STATUS DATE	2026-04-03
GENERATED	2026-10-29 23:14
PRIMARY EAC METHOD	typical, BAC ÷ CPI
TASKS	12

CONTENTS

1. KPI summary
2. Charts
3. Task table
4. Insights
5. Unusual expenses
6. AI summary
7. Snapshot history
8. Formula appendix

KPI summary

Project totals as of 2026-04-03. Status follows the indicator rules (§5); amounts in PKR.


Metric	Value	Status
Budget at completion (BAC)	PKR 1,040,000.00	—
Planned value (PV)	PKR 522,926.41	—
Earned value (EV)	PKR 496,000.00	—
Actual cost (AC)	PKR 570,000.00	—
Cost variance (CV)	-PKR 74,000.00	Action needed
Schedule variance (SV)	-PKR 26,926.41	Watch
CV%	-14.92%	Action needed
SV%	-5.15%	Watch
Cost performance index (CPI)	0.87	Action needed
Schedule performance index (SPI)	0.95	Watch
Estimate at completion (EAC, typical, BAC ÷ CPI)	PKR 1,195,161.29	Action needed
Estimate to complete (ETC)	PKR 625,161.29	—
Variance at completion (VAC)	-PKR 155,161.29	Action needed
To-complete performance index (TCPI)	1.16	Action needed
% complete	47.69%	—
% spent	54.81%	—

Charts

The dashboard charts at the time of export.


S-curve

Cumulative planned value (dotted), earned value and actual cost over time, with the budget and the forecast at completion.

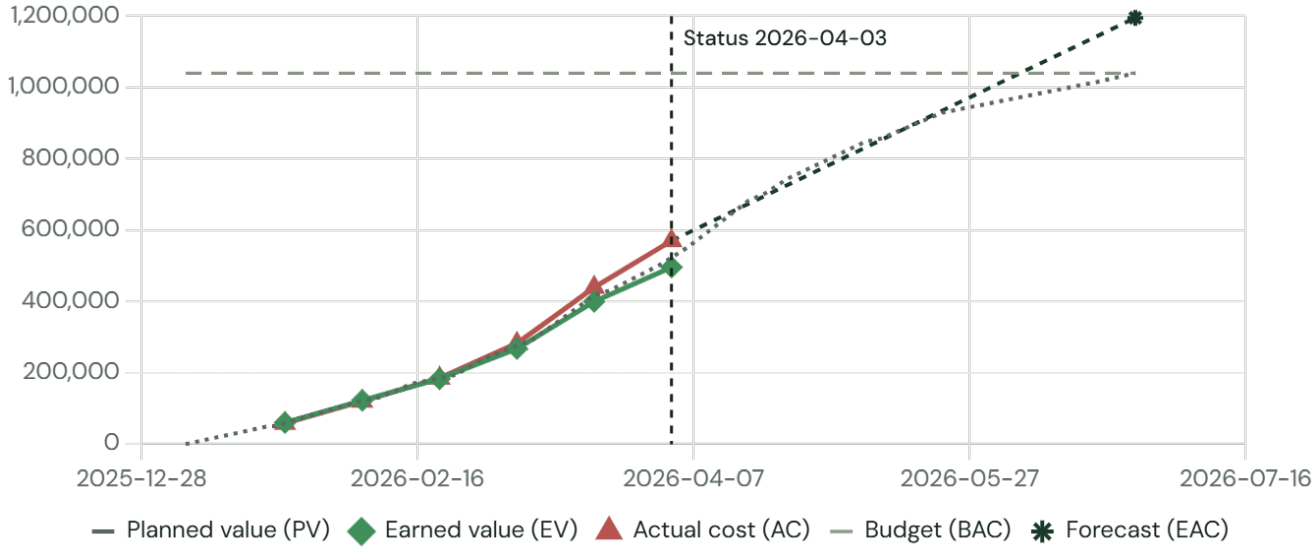


Estimated vs actual cost

Budget (outlined) compared with actual cost (solid) for each task.

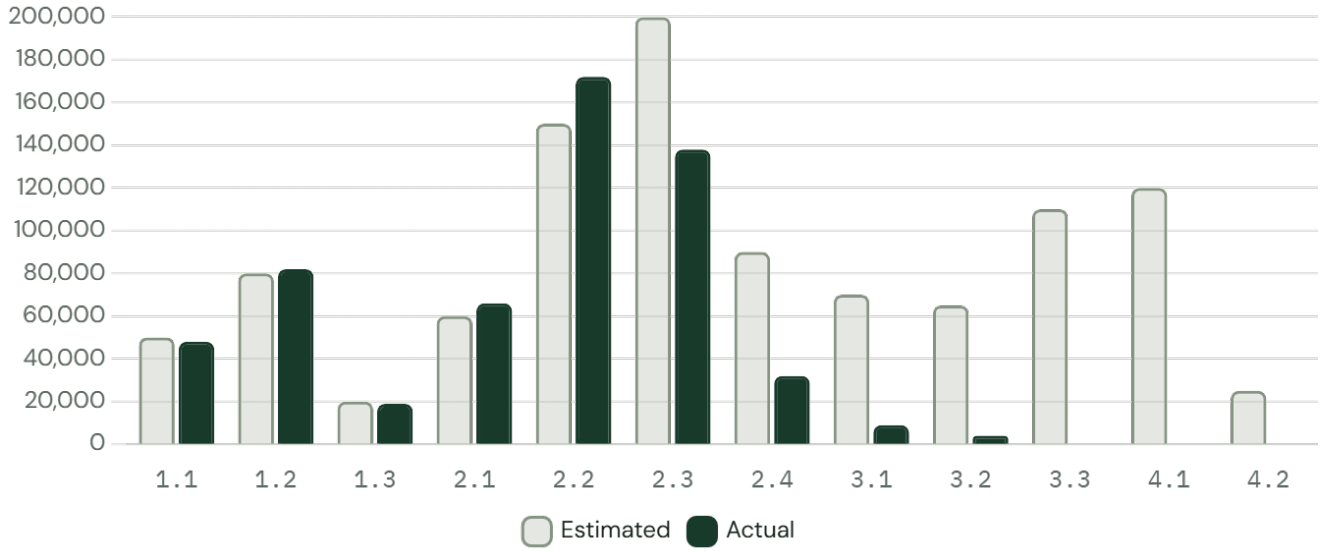


CPI and SPI trend

Cost (CPI, solid) and schedule (SPI, dashed) efficiency at each status update; 1.00 is on target.

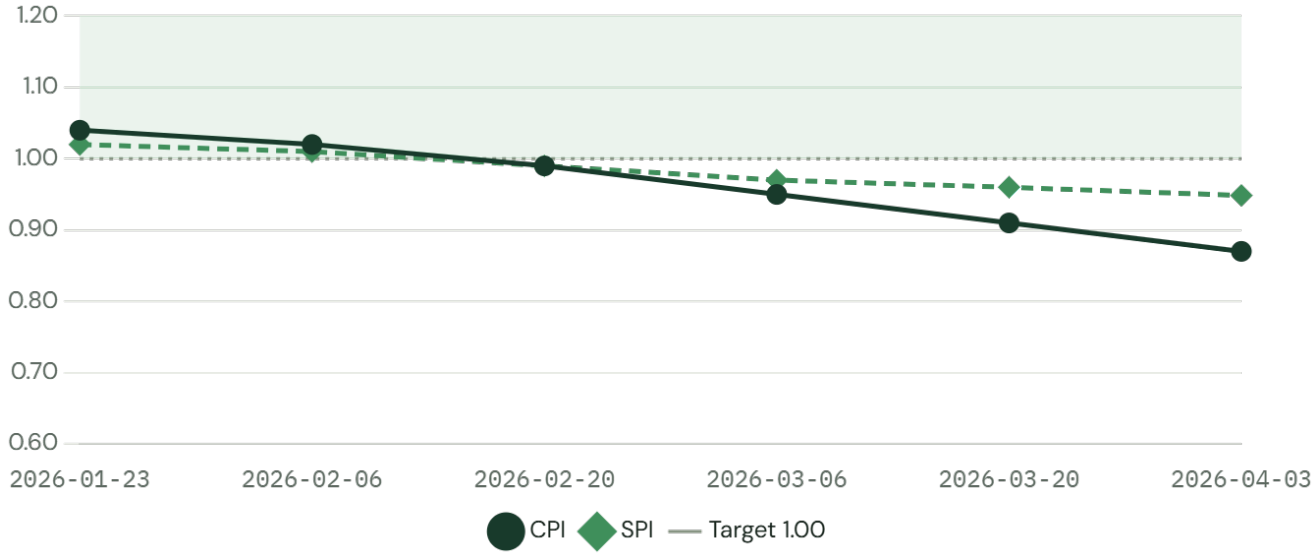

Cost variance by category

Earned value minus actual cost per cost category; bars to the left are overruns.

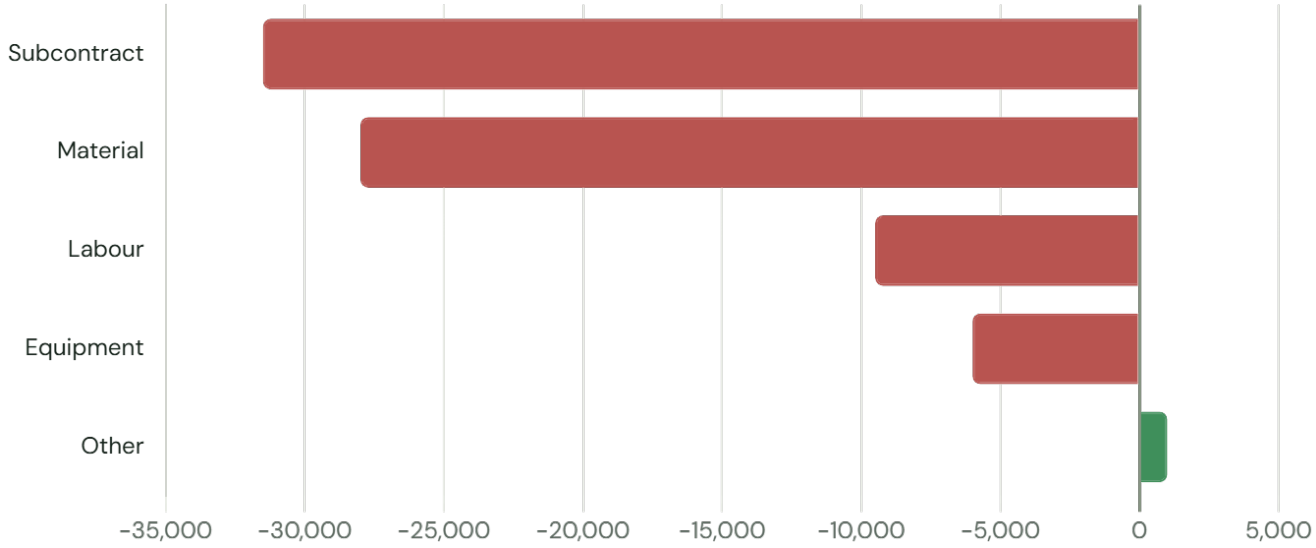

Task table

Estimated cost is the task budget; variance = estimated - actual. Amounts in PKR; negative values in red.

Task ID	Name	Estimated	Actual	Variance	% Var.	EV	CPI	SPI
1.1	Requirements	50,000.00	48,000.00	2,000.00	4.00%	50,000.00	1.04	1.00
1.2	Design	80,000.00	82,000.00	-2,000.00	-2.50%	80,000.00	0.98	1.00
1.3	Permits	20,000.00	19,000.00	1,000.00	5.00%	20,000.00	1.05	1.00
2.1	Site preparation	60,000.00	66,000.00	-6,000.00	-10.00%	60,000.00	0.91	1.00
2.2	Foundations	150,000.00	172,000.00	-22,000.00	-14.67%	150,000.00	0.87	1.00
2.3	Structural steel	200,000.00	138,000.00	62,000.00	31.00%	110,000.00	0.80	0.86

Task ID	Name	Estimated	Actual	Variance	% Var.	EV	CPI	SPI
2.4	Masonry	90,000.00	32,000.00	58,000.00	64.44%	22,500.00	0.70	0.73
3.1 !	Electrical rough-in	70,000.00	9,000.00	61,000.00	87.14%	3,500.00	0.39	0.92
3.2 !	Plumbing rough-in	65,000.00	4,000.00	61,000.00	93.85%	0.00	0.00	N/A
3.3	Roofing	110,000.00	0.00	110,000.00	100.00%	0.00	N/A	N/A
4.1	Interior finishes	120,000.00	0.00	120,000.00	100.00%	0.00	N/A	N/A
4.2	Handover and commissioning	25,000.00	0.00	25,000.00	100.00%	0.00	N/A	N/A
Total (12 tasks)		1,040,000.00	570,000.00	470,000.00	45.19%	496,000.00	0.87	0.95

"!" marks a task with an unusual expense (see Unusual expenses).

Insights

Indicator rules from §5 that are triggered, most serious first.

Rule	Status	Finding	What to do
IN-03	Action needed	Significant cost overrun: each 1 unit spent earns only 0.87 of value (CPI 0.87).	Hold a cost review now: find the overrunning tasks, cut non-essential spend and agree corrective actions.
IN-09	Action needed	Recovering to budget is unrealistic: the remaining work would need a TCPI of 1.16 (more than 1.10). Consider re-baselining to the EAC of PKR 1,195,161.29.	Finishing on budget is unlikely. Agree a new budget (re-baseline) using the EAC with stakeholders.
IN-10	Action needed	Forecast overrun of PKR 155,161.29 (14.92%) at completion.	Report the forecast overrun to stakeholders and plan how it will be funded or reduced.
IN-05	Watch	Slightly behind schedule: only 94.85% of the planned work is done (SPI 0.95).	Look at the tasks that are behind plan and whether extra resources or re-sequencing can help.
IN-11	Watch	Cost efficiency is trending down: CPI fell for 3 consecutive snapshots (0.99 -> 0.95 -> 0.91 -> 0.87).	Find out what changed in recent periods before the trend becomes a large overrun.
IN-12	For information	Main contributors to overrun: 2.3 Structural steel (CV -PKR 28,000.00), 2.2 Foundations (CV -PKR 22,000.00), 2.4 Masonry (CV -PKR 9,500.00).	Start with these tasks: they explain most of the overrun.

Unusual expenses

Deterministic checks AN-01…AN-06 on task costs and status history.

Rule	Task / date	Severity	Reason
AN-01	Task 3.1	High	Task 3.1 has a cost variance of -157.14%, far from the other tasks (average -30.37%, z-score -2.53).
AN-02	Task 3.2	Medium	Task 3.2 has spent PKR 4,000.00 but is 0% complete.

AI summary

Generated offline (rule-based) · Generated 2026-10-29 23:14 · AI service not configured

EXECUTIVE SUMMARY

Clinic Building Extension is 47.69% complete and has spent 54.81% of its PKR 1,040,000.00 budget as of 2026-04-03. The project is significantly over budget (CPI 0.87). Work is slightly behind schedule (SPI 0.95). The forecast at completion is PKR 1,195,161.29, an overrun of PKR 155,161.29 (14.92%). 2 unusual expenses were flagged (1 high severity).

KEY RISKS

- Significant cost overrun: each 1 unit spent earns only 0.87 of value (CPI 0.87).
- Recovering to budget is unrealistic: the remaining work would need a TCPI of 1.16 (more than 1.10). Consider re-baselining to the EAC of PKR 1,195,161.29.
- Forecast overrun of PKR 155,161.29 (14.92%) at completion.
- Slightly behind schedule: only 94.85% of the planned work is done (SPI 0.95).

RECOMMENDATIONS

1. Hold a cost review now: find the overrunning tasks, cut non-essential spend and agree corrective actions.
2. Finishing on budget is unlikely. Agree a new budget (re-baseline) using the EAC with stakeholders.
3. Report the forecast overrun to stakeholders and plan how it will be funded or reduced.

Snapshot history

Cumulative values at each recorded status update (PKR).

Date	PV	EV	AC	CV	SV	CPI	SPI
2026-01-23	59,066.67	60,248.00	57,931.00	2,317.00	1,181.33	1.04	1.02
2026-02-06	121,200.00	122,412.00	120,012.00	2,400.00	1,212.00	1.02	1.01
2026-02-20	184,736.84	182,889.00	184,736.00	-1,847.00	-1,847.84	0.99	0.99
2026-03-06	276,000.00	267,720.00	281,811.00	-14,091.00	-8,280.00	0.95	0.97
2026-03-20	416,410.26	399,754.00	439,290.00	-39,536.00	-16,656.26	0.91	0.96
2026-04-03	522,926.41	496,000.00	570,000.00	-74,000.00	-26,926.41	0.87	0.95

Formula appendix

How each metric is calculated. "N/A" means a value cannot be calculated (e.g. division by zero).

Metric	Formula	Meaning
BAC — Budget at completion	Sum of task budgets	The total approved budget for all the work.
PV — Planned value	budget × share of planned duration elapsed by the status date	How much work, in money, should have been done by now according to the plan.
EV — Earned value	budget × % complete ÷ 100	The budgeted value of the work actually done.
AC — Actual cost	Sum of actual cost to the status date	What the work done so far has actually cost.

Metric	Formula	Meaning
Variance — Cost variance (simple)	estimated cost - actual cost	Budget left over (positive) or overspent (negative), ignoring progress.
CV — Cost variance	EV - AC	Positive: the work done cost less than its value. Negative: it cost more.
SV — Schedule variance	EV - PV	Positive: ahead of plan. Negative: behind plan (in money terms).
CV% — Cost variance %	CV ÷ EV × 100	Cost variance as a share of the value earned.
SV% — Schedule variance %	SV ÷ PV × 100	Schedule variance as a share of the planned work.
CPI — Cost performance index	EV ÷ AC	Value earned per 1 unit spent. Above 1.00 is under budget; below 1.00 is over.
SPI — Schedule performance index	EV ÷ PV	Share of the planned work that is done. Above 1.00 is ahead; below 1.00 is behind.
EAC — Estimate at completion (typical)	BAC ÷ CPI	Forecast final cost if the current cost efficiency continues.
EAC — Estimate at completion (atypical)	AC + (BAC - EV)	Forecast final cost if the overrun so far was a one-off and the rest goes to plan.
EAC — Estimate at completion (combined)	AC + (BAC - EV) ÷ (CPI × SPI)	Forecast final cost when both cost and schedule performance affect the rest.
ETC — Estimate to complete	EAC - AC	How much more the remaining work is expected to cost.
VAC — Variance at completion	BAC - EAC	Expected saving (positive) or overrun (negative) at the end.
VAC% — Variance at completion %	VAC ÷ BAC × 100	Expected saving or overrun as a share of the budget.
TCPI — To-complete performance index	(BAC - EV) ÷ (BAC - AC)	Cost efficiency the remaining work needs to finish on budget. Above 1.10 is unrealistic.
% complete — Percent complete	EV ÷ BAC × 100	Share of the total work that is done.
% spent — Percent spent	AC ÷ BAC × 100	Share of the total budget that has been spent.
